
DAVIS ROAD BRIDGE REPLACEMENT AND ROAD WIDENING PROJECT

Monterey County Department of Public Works, Parks & Facilities August 3, 2022

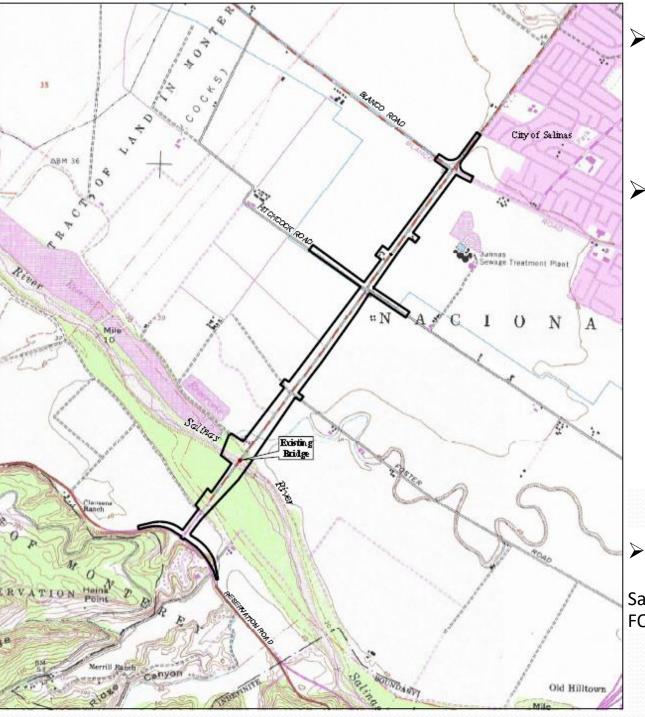



Project Limits
Blanco Road to Reservation Road


Project Elements

- 1. All weather crossing over Salinas River
- 2. Four-lane Davis Road
- 3. Roundabout at Reservation/Davis Intersection
- 4. Class II bike lanes along Davis Road
- 5. Bus Queue jump lane at Davis Rd/Blanco Rd
- 6. Intersection improvements at Foster and Hitchcock
- Regional Transportation Plan Consistency
 Salinas-Marina Multimodal Corridor
 FORA Base Re-use Plan



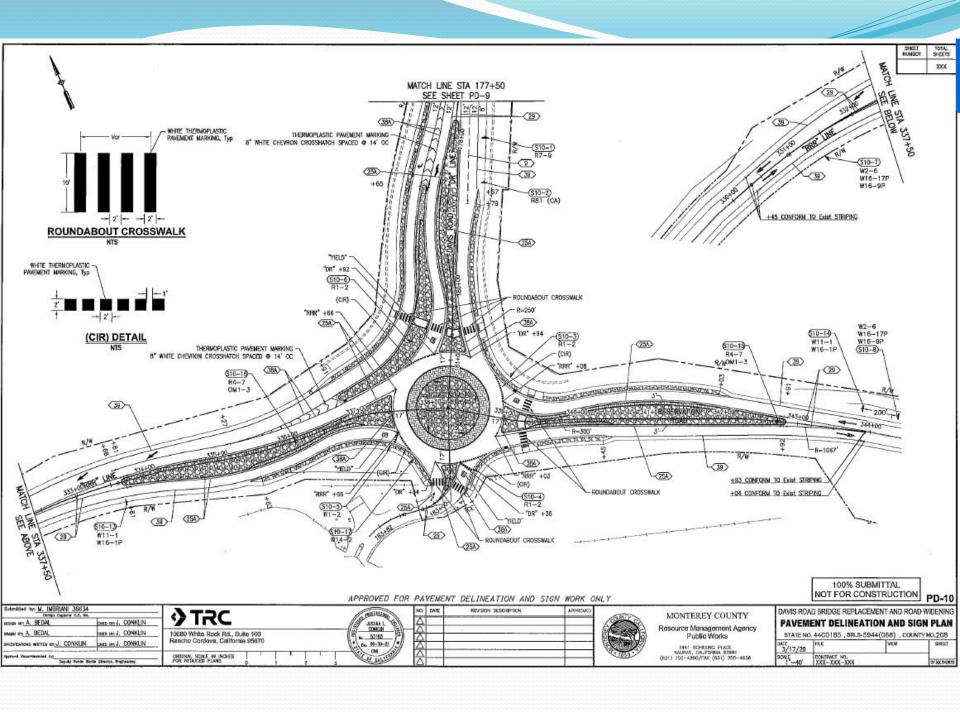

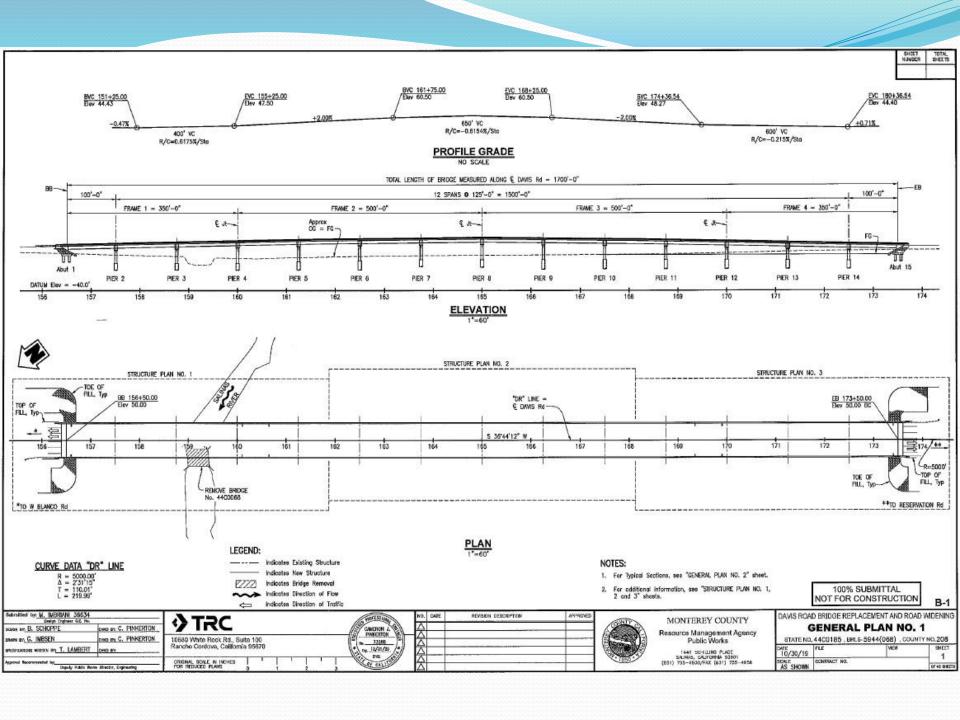

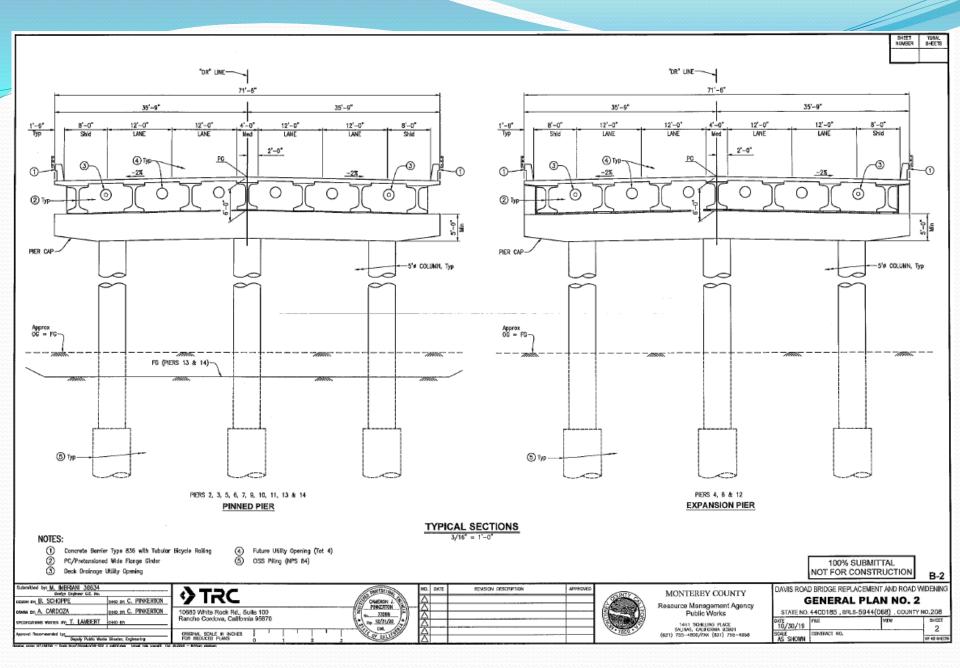

Project Status

1. Work Status.

- Final Design 95% complete
- Coordinating with impacted utility companies
- Negotiating road and construction easements
- Acquiring regulatory permit applications

2. Schedule

- Fall 2022: Complete R/W phase
- Spring 2023: Utility relocations
- Fall 2023: Start Construction
- Fall 2025: Complete construction

Project Status (Con't)

3. Funding

- > Total Project Estimate \$72.5 million
- ➤ Bridge component \$45 million
 - FHWA Highway Bridge Program (88%)
 - Local Funds for federal match (RSTP, Gas Tax)
- Road Widening (\$27.5 M)
 - Local Funds
 - EG development fees (\$1.3M)
 - FORA funds (\$1.8 million)
 - Other grants or impact fees

4. Project Risks

- Complete project funding
 - Grants
 - FORA
- R/W issues
- Utility relocation delays
